

Work Order ID 141268

February 03, 2016 10:24:40 AM

141268

Shortage. Rush ASAP
Cut Feb 10

Page 1

Item ID: D4011-1 Accept *N9000040100* Setup Start *NS1*
Revision ID: Stop *NS2*
Item Name: Clamp, Short
Start Date: 2/3/2016 Start Qty: 60.00 *60* Cust Item ID:
Required Date: 2/12/2016 Req'd Qty: 60.00 *60* Customer:
Reference:

Approvals: Process Plan: SHA Date: 20160207 Tooling: _____ Date: _____ Run Start *NR1*
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
Draw Nbr	Revision Nbr								
D4011	C								
100	PURCHASING	0.00							
100									
Waterjet	Memo	0.05							
FLOW CNC Waterjet	1-Cut as per Dwg								
	Dwg Rev: <u>C</u>								
	Prog Rev: <u>C</u>								
	2-Deburr if necessary								
110	QC2- Inspect parts off machine FAI/FAIB	0.00							
110									
QC	Memo	0.01							
Quality Control									

75

2/16/02/10

75

2/16/02/10

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QS1042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
		OTHER : ☐							

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐		Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐					
OTHER : ☐									

Work Order ID 141268

February 03, 2016 10:24:40 AM

141268

Page 3

Item ID: D4011-1 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Clamp, Short
Start Date: 2/3/2016 Start Qty: 60.00 ***60*** Cust Item ID:
Required Date: 2/12/2016 Req'd Qty: 60.00 ***60*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
150	Identify as per dwg & Stock Location: <u>ST544</u>	0.00							
150						75		248 6 300	FEB 16 2016
Packaging	Memo	0.01							
Packaging									
160	QC21- Final Inspection - Work Order Release	0.00							
160									
QC	Memo	0.10							
Quality Control									

_____ MCS _____ FEB 16 2016

MCS FEB 16 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
		OTHER : ☐			

Picklist Print

Februdry 03, 2016 10:24:46 AM

Page 1

Work Order ID: 141268

141268

Parent Item: D4011-1

D4011-1

Parent Item Name: Clamp, Short

Start Date: 2/3/2016

Required Date: 2/12/2016

Start Qty: 60.00

Required Qty: 60.00

Comments: IPP RevA: New issue DD verified by:EC
11.05.19 MADE IN HOUSE DD verified by:EC

IPP Rev:B

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
M304S14GA		Purchased				100	sf	69.8000	0.07	4.421053			

M304S14GA

304SS sheet .080

02/16/03/10

Location

Loc Qty

Loc Code



MAT019

69.8

M129972

69.8

6

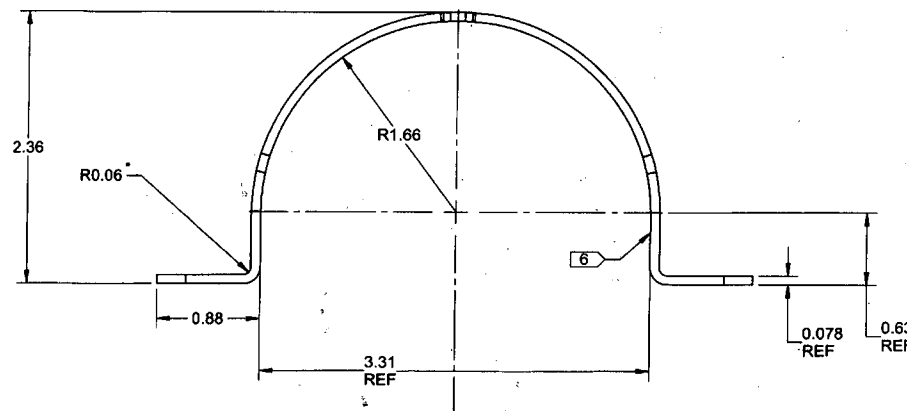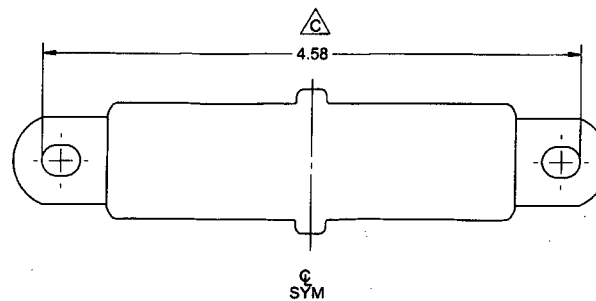

D4011-1 CLAMP, SHORT

RELEASED

2015 MAR 26

4P EN 15-332


20160203
SA 141268

REV.	DESCRIPTION	BY	DATE
C	ADD SLOT HOLES, ADD CUSHION RETENTION DETAILS TO -1/-3/-5 CLAMPS, REASON: PAR 14-331, NCR 14-3521, PAR 14-388; ZND5-1, A8-1, B6-2, B2-2, D4-3, A8-3, B6-4, B2-4, D5-5, A8-5, B6-6, B2-6, REVISE NOTE 6; ZN A8-2, A8-4, A8-6	VS	14.09.22
B	SHORTEN HEIGHT OF -1/-3 CLAMPS BY 0.125; ADDED -5. REASON: PROVIDE MORE CLEARANCE UPON INSTALLATION ON OEM SKIDTUBES	MB	09.11.11
A	NEW ISSUE	MB	09.10.21
DESIGN	VS	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA DRAWING NO. D4011 CLAMP THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS BANNED ON THE OPENED CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	
DRAWN	VS		
CHECKED	RF		
MFG. APPR.	DD		
APPROVED	HS		
DE APPR.	DS	CLAMP DATE 14.09.22	
APPROVED		CLAMP DATE 14.09.22	




NOTES:

- 1) MATERIAL: MAKE FROM D4011-1F
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: IDENTIFY WITH DART P/N "D4011-1" AND B/N PER QSI 044 6.1 (PERMANENT MARKER)
- 7) WEIGHT: 0.02 lbs

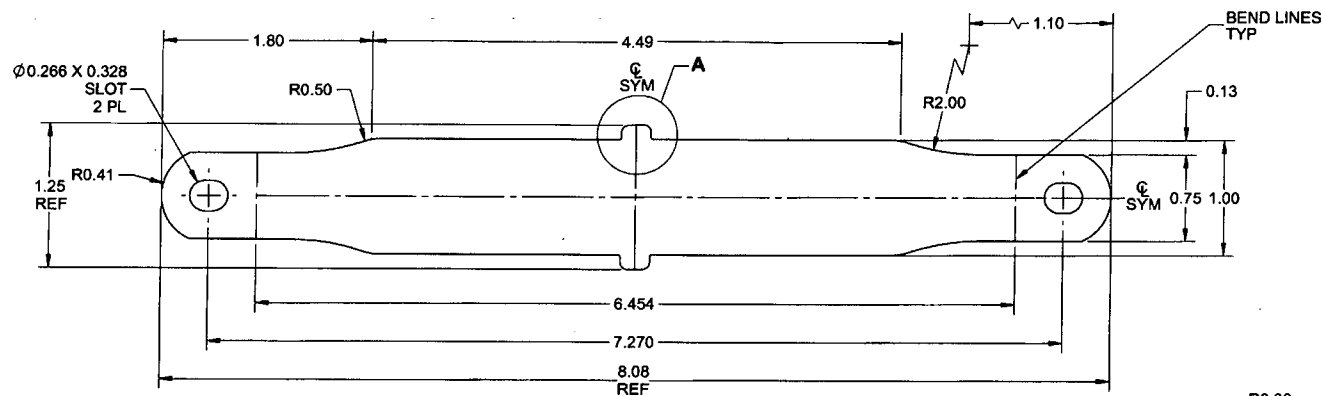

D4011-1F CLAMP, FLAT PATTERN SHORT



DETAIL A
SCALE 2X
2 PL

RELEASED



2015 MAR 26

NOTES:

- 1) MATERIAL: AISI 304/316 STAINLESS STEEL SHEET ANNEALED 2B FINISH, 14 GAUGE (0.078 THICK)
PER AMS 5513 (304) OR 5524 (316) OR ASTM A240 OR ASME SA240
REF. DART SPEC. M304S14GA
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: N/A
- 7) WEIGHT: 0.02 lbs
- 8) FOR UNDIMENSIONED DETAILS, REFER TO FLAT PATTERN CAD FILE D4011-1F-RevC.DXF

APPROVED

DESIGN	VS	DART AEROSPACE LTD	
DRAWN	VS	HAWKESBURY, ONTARIO, CANADA	
CHECKED	RF	DRAWING NO.	REV. C
MFG. APPR.	DD	D4011	SHEET 2 OF 6
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	CLAMP	NTS
DATE	14.09.22	COPYRIGHT © 2014 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			

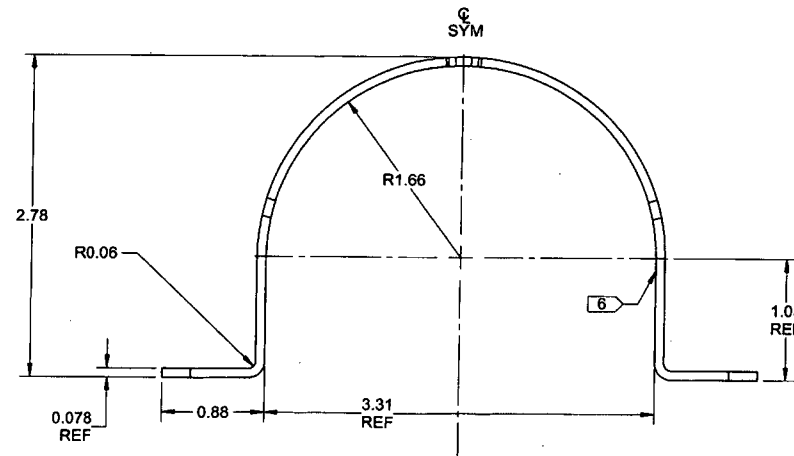

D4011-3 CLAMP, LONG

20160203


RELEASED


2015 MAR 26

APPROVED


DESIGN	VS	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	VS		
CHECKED	RF	DRAWING NO.	REV. C
MFG. APPR.	DD	D4011	SHEET 3 OF 6
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	CLAMP	NTS
DATE	14.09.22	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

- NOTES:**
- 1) MATERIAL: MAKE FROM D4011-3F
 - 2) FINISH: NONE
 - 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
 - 4) UNITS: INCHES UNLESS OTHERWISE NOTED
 - 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
 - 6) IDENTIFICATION: IDENTIFY WITH DART P/N "D4011-3" AND B/N PER QSI 044 6.1 (PERMANENT MARKER)
 - 7) WEIGHT: 0.02 lbs



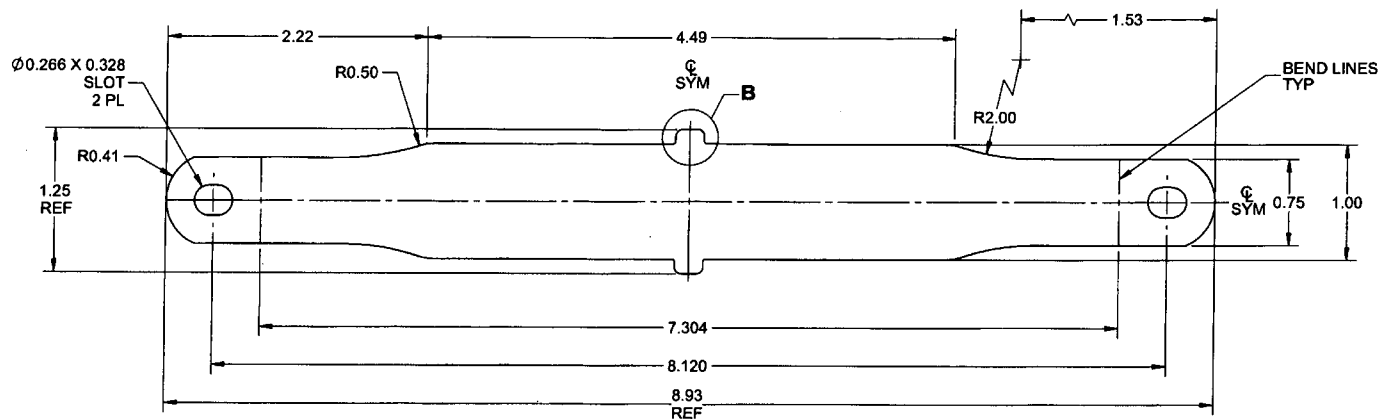

D4011-3F CLAMP FLAT PATTERN, LONG



DETAIL B
SCALE 2X
2 PL

RELEASED



2015 MAR 26

NOTES:

- 1) MATERIAL: AISI 304/316 STAINLESS STEEL SHEET ANNEALED 2B FINISH, 14 GAUGE (0.078 THICK)
PER AMS 5513 (304) OR 5524 (316) OR ASTM A240 OR ASME SA240
REF. DART SPEC. M304S14GA
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: N/A
- 7) WEIGHT: 0.02 lbs
- 8) FOR UNDIMENSIONED DETAILS, REFER TO FLAT PATTERN CAD FILE D4011-3F-RevC.DXF

APPROVED

DESIGN	VS	DART AEROSPACE LTD	
DRAWN	VS	HAWKESBURY, ONTARIO, CANADA	
CHECKED	RF	DRAWING NO.	REV. C
MFG. APPR.	DD	D4011	SHEET 4 OF 6
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	CLAMP	NTS
DATE	14.09.22	COPYRIGHT © 2014 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL, AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			

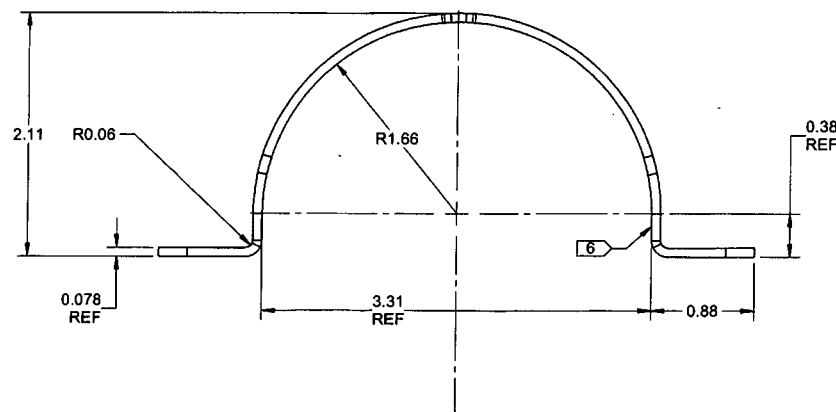

D4011-5 CLAMP, SHORT (OEM)

RELEASED

2015 MAR 26 *up*


APPROVED

DESIGN	VS	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	VS		
CHECKED	RF	DRAWING NO.	REV. C
MFG. APPR.	DD	D4011	SHEET 5 OF 6
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	CLAMP	NTS
DATE	14.09.22	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	




NOTES:

- 1) MATERIAL: MAKE FROM D4011-5F
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: IDENTIFY WITH DART P/N "D4011-5" AND B/N PER QSI 044 6.1 (PERMANENT MARKER)
- 7) WEIGHT: 0.02 lbs

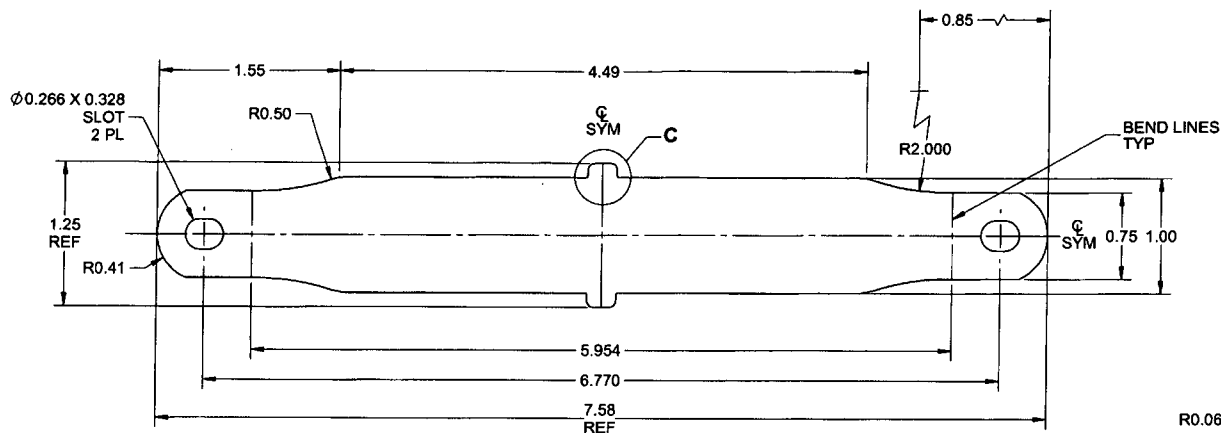

D4011-5F CLAMP, FLAT PATTERN, SHORT (OEM)



DETAIL C
SCALE 2X

RELEASED

2015 MAR 26

NOTES:

- 1) MATERIAL: AISI 304/316 STAINLESS STEEL SHEET ANNEALED 2B FINISH, 14 GAUGE (0.078 THICK)
PER AMS 5513 (304) OR 5524 (316) OR ASTM A240 OR ASME SA240
REF. DART SPEC. M304S14GA
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: N/A
- 7) WEIGHT: 0.02 lbs
- 8) FOR UNDIMENSIONED DETAILS, REFER TO FLAT PATTERN CAD FILE D4011-5F-RevC.DXF

APPROVED

DESIGN	VS	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	VS		
CHECKED	RF	DRAWING NO.	REV. C
MFG. APPR.	DD	D4011	SHEET 6 OF 6
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	CLAMP	NTS
DATE	14.09.22	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

